

Hardware Emulation Projects 2002

April 22, 2002

sched_ikos_2002_11.xls

Project	Size	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
R300	15M	2	2	2	2					Colin/Herbert
RV250	10M	2	2	2	2					Jaroslav/Ron
A5	11M	2	2	2	2	2	2	2	2	Bill/Evgeny
X220/5	8M	1	1	1	1	1	1	1	1	Herbert/Paul
X300							1	1	1	
RV350	15M				2	2	2	2	2	Colin/Jaro
R400 emulator evaluation		1	1	1						Ron/Colin/Jaroslav
R400	25M				2	2	2	2	2	Ron
R400Disp	5M						1	1	1	
FPGA Tool evaluation/devel			1	1	1	1	1	1	1	
PCB Creation		1	1	1	1					
PC Farm maintenance		0.5	0.5	0.5	0.5	0.5	0.5	0.5	0.5	Herbert

Total personnel required	9.5	10.5	10.5	13.5	8.5	10.5	10.5	10.5	10.5
Total personnel available	6	6	6	6	6	6	6	5	5
Additional personnel required:	3.5	4.5	4.5	7.5	2.5	4.5	5.5	5.5	5.5

Hardware Emulation Project Allocation


Box	Type	No Brds	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
IKOS1	VLE5M	6	R300	R300	R300	RV350	RV350	R400D	R400D	R400D
IKOS2	VLE5M	6	R300	R300	R300	RV350	RV350	RV350	RV350	RV350
IKOS3	VLE5M	6	R300	R300	R300	RV350	RV350	RV350	RV350	RV350
IKOS4	VLE5M	6	RV250	RV250	RV250	X225	X225	X225	X225	X225
IKOS5	VLE5M	5	RV250	RV250	RV250	X225	X225	X225	X225	X225
IKOS6	VLE5M	6	X225	X225	X225	X225	X225	X300	X300	X300
IKOS7	VLE5M	2	X225	X225	X225	X225	X225	X300	X300	X300
IKOS8	VLE15M	9	R300	RV250	A5	A5	A5	A5	A5	A5
??	??					R400	R400	R400	R400	R400

AMD1044_0228487

ATI E
IDP

March 12th, 2003

Hardware Emulator Allocation

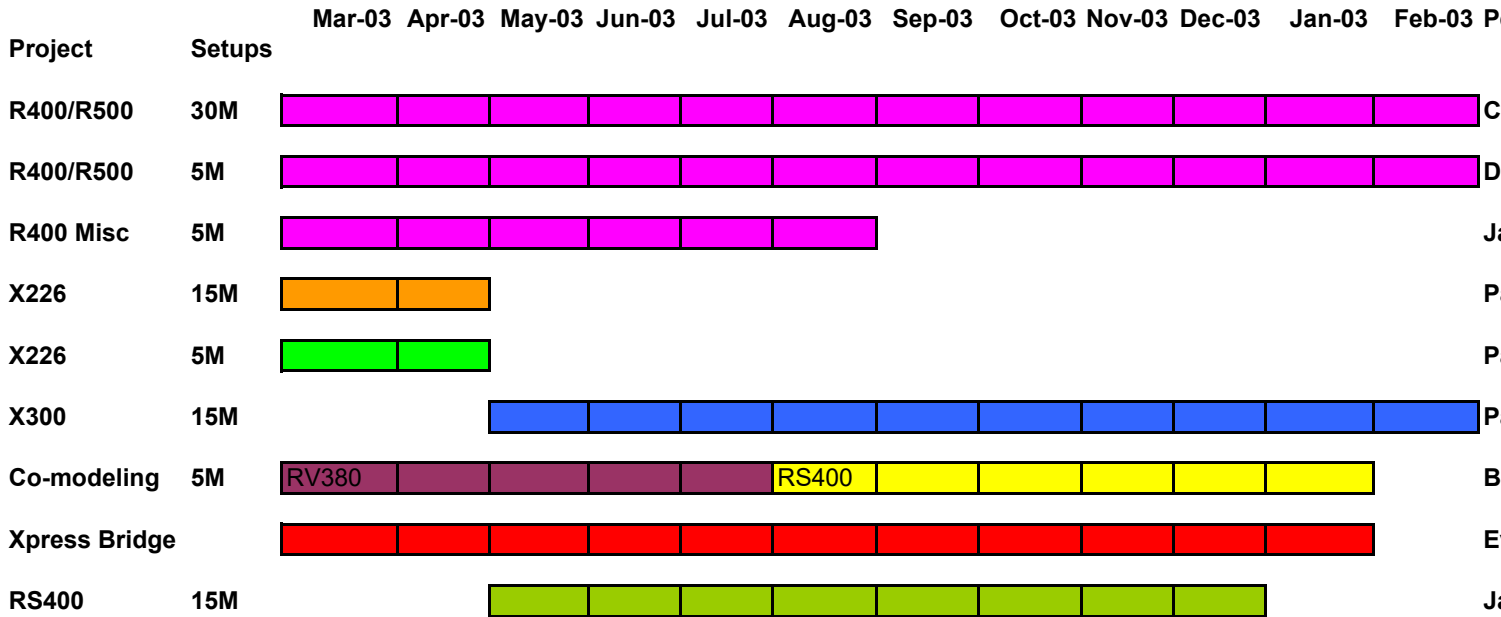

7-Jun-04

Hardware Emulator Allocation		Aug-04	Sep-04	Oct-04	Nov-04	Dec-04	
Project	Setups						
Xenos/Xbox EP	30M share						Colin
Xenos/Xbox NB	60M						Evgeny
SB400 PCB							Evgeny
Rialto	30M share						Herbert
T520	15M share						Bill
X250	Palladium						Paul
RS600	30M share						Herbert
UDC	15M share						Bill
RN50	15M share						Ron

46
